


WATERFRONT 2019 WORK PLAN

March 6, 2019
City of Seattle, Office of the Waterfront and Civic Projects

WATERFRONT SEATTLE PROGRAM



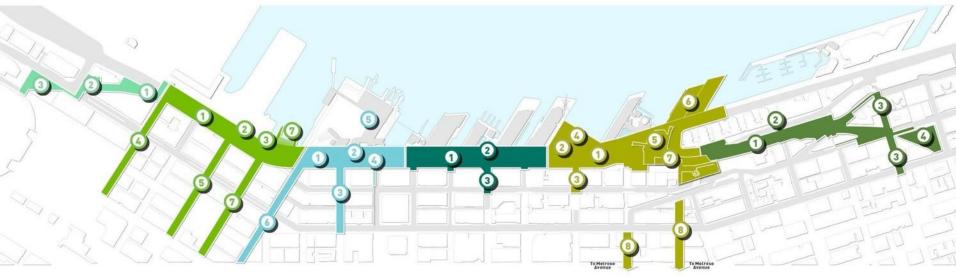

RAILROAD WAY	PIONEER SQUARE	TRANSIT HUB	HISTORIC PIERS	CENTRAL PUBLIC SPACE	BELLTOWN
1 WATERFRONT	1 ALASKAN WAY	1 ALASKAN WAY	1 ALASKAN WAY	1 ELLIOTT WAY	1 ELLIOTT WAY
2 PIONEER SQUARE 3 STADIUMS	WATERFRONT PROMENADE	2 WATERFRONT PROMENADE	2 WATERFRONT PROMENADE	2 WATERFRONT PROMENADE	UNION ST. WATERFRONT PARK REBUILD OCEAN PAVILION 3 BELL ST. PORTAL PARK
	3 WASHINGTON ST. BOAT LANDING 4 S. KING ST. 5 S. MAIN ST.	3 COLUMBIA ST. MARION ST. PEDESTRIAN BRIDGE COLMAN DOCK	3 SENECA ST.	 UNION ST. WATERFRONT PARK REBUILD OCEAN PAVILION PIERS 62/63 PHASE 1 REBUILD 	
	S. WASHINGTON ST. HABITAT INTERTIDAL ZONE	TERMINAL REPLACEMENT (5) YESLER WAY		OVERLOOK WALK PIKE/PINE STS.	⊙ 500 ft.

2018-2019 ACCOMPLISHMENTS



- MOU with Aquarium Society to advance Ocean Pavilion (July 2018)
- Main Corridor plans completed and out to bid (2018)
 - Bid package finalized, advertised in November 2018
 - Majority of ROW acquisitions and permitting completed
- Key early construction advanced on time and on budget
 - "Early works" utility relocations and areaway modifications
 - Pier 62 Rebuild
 - Marine habitat enhancements south of Colman Dock
- Partnership agreement between Seattle Parks and Friends of Waterfront Seattle (January 2019)
- Waterfront Local Improvement District (LID) formed (January 2019)


2019 LOOK AHEAD



- Start Main Corridor construction
 - Anticipated for August 1, 2019, with limited construction on Columbia Street beginning mid-July
 - 3-4 month delay due to viaduct demolition shifts overall waterfront completion to Fall 2023
- Local Improvement District (LID)
 - Adopt Final Assessment Roll resolution (late-2019; starts individual assessment hearing process)
- Complete 30% designs for Pike and Pine streets, Pioneer Square streets
- Complete 60% design for Overlook Walk
- Establish Pilot Agreement with Friends and Parks for Management of Pier 62
- Complete Pier 62 construction by end of 2019

CONSTRUCTION SCHEDULE



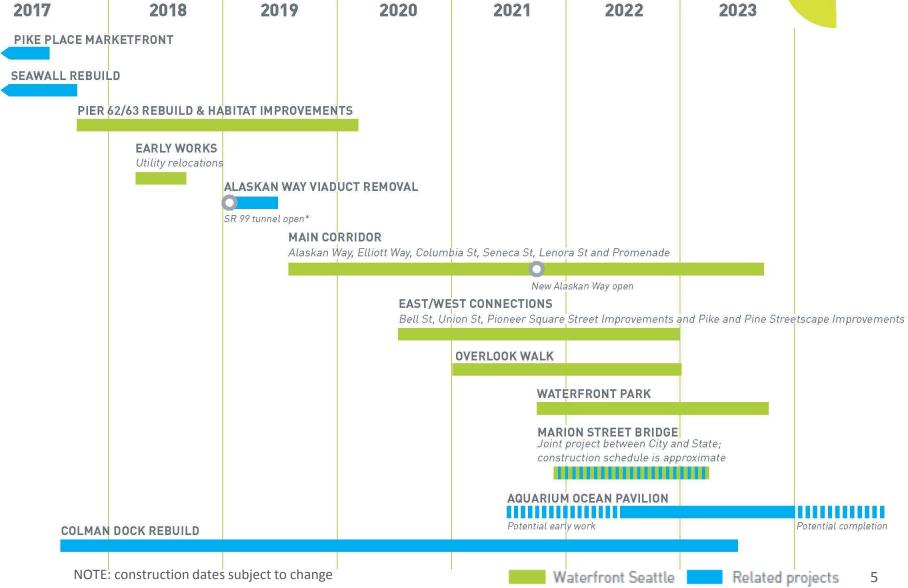

WATERFRONT CONSTRUCTION: CORE VALUES





- Ensure access for businesses, residents, and all modes of travel
- Support operations for BNSF,
 Port, and Colman Dock ferries
- Maintain major utility services
- Support access to parking and transit during construction
- Coordination with all public and private projects


CONSTRUCTION COMMUNICATIONS



SEATTLE WATERFRONT CONSTRUCTION Major construction projects: 2018-2023 What's Happening What's Ahead Travelers' Information Contact Us

Welcome to the Seattle waterfront construction information site!

Seattles Central Waterfront is going to be a busy place over the next several years, with multiple construction projects underway. To make it easy for you to stay up to date on what's going on and what's ahead, we've compiled project information all one place. This site provides general information about current and future public projects. For additional project details, visit the project websites, which can be found in the "Contact Us" page.

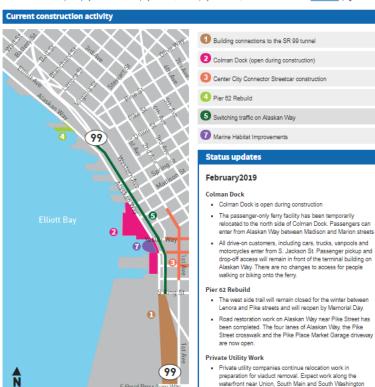

streets. Work will be primarily in small areas, and with relatively short durations of single-lane closures and localized

. See the map of the private utility work in the area.

- Early briefings to most affected stakeholders
- "Street team" outreach approach
 - Advanced notifications
 - 24-hour hotline
 - Email updates
 - On-the-ground outreach
- Continue updating multi-agency waterfront construction portal: waterfrontconstruction.org
