

# Ship Canal Water Quality Project

## Project Cost Update

Civil Rights, Utilities, Economic Development & Arts Committee

*May 22, 2018*

Seattle Public Utilities



**City of Seattle**

# Ship Canal Water Quality Project

- Project overview
- Cost reconciliation and review process
- Potential scope adjustments
- Revised cost estimate
- Next steps



# Ship Canal Water Quality Project

## Consent decree


- With US Department of Justice, US Environmental Protection Agency, and WA Department of Ecology
- Less than 1 combined sewer overflow per outfall per year on a 20-year moving average

## Joint Project


- Outfalls: 2 KC, 5 Seattle
- Four projects reduced to one
- Reduced community impacts
- Improved operational flexibility

## Joint Project Agreement

- 12/8/2015: City of Seattle – 65%
- 6/21/2016: King County – 35%

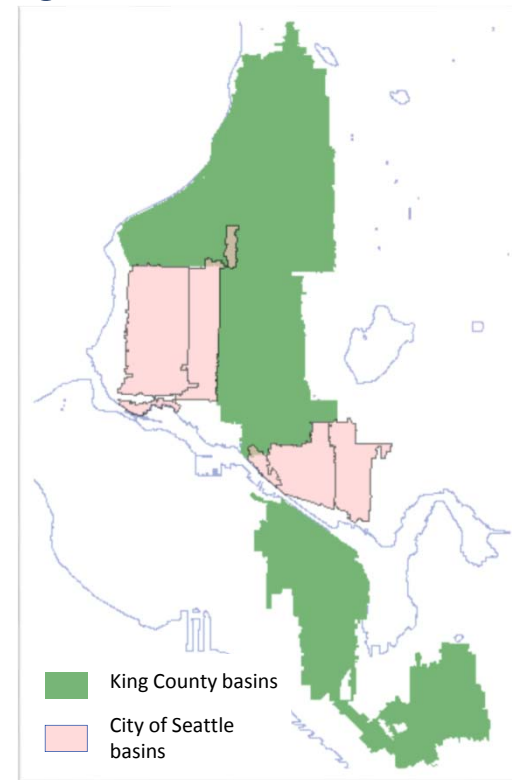

# 2017 Combined Sewer Overflows

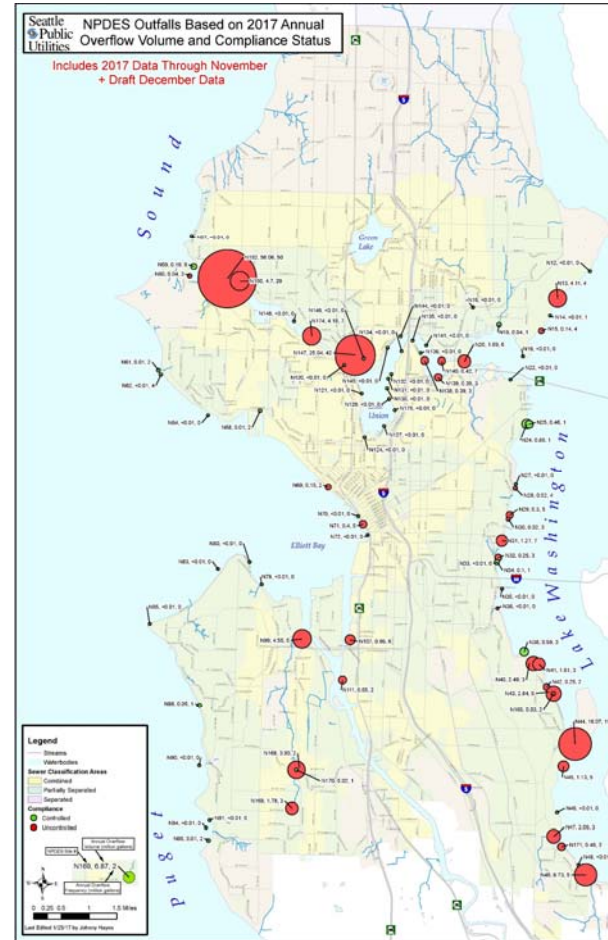




Seattle Public Utilities





King County

# Ship Canal Water Quality Project


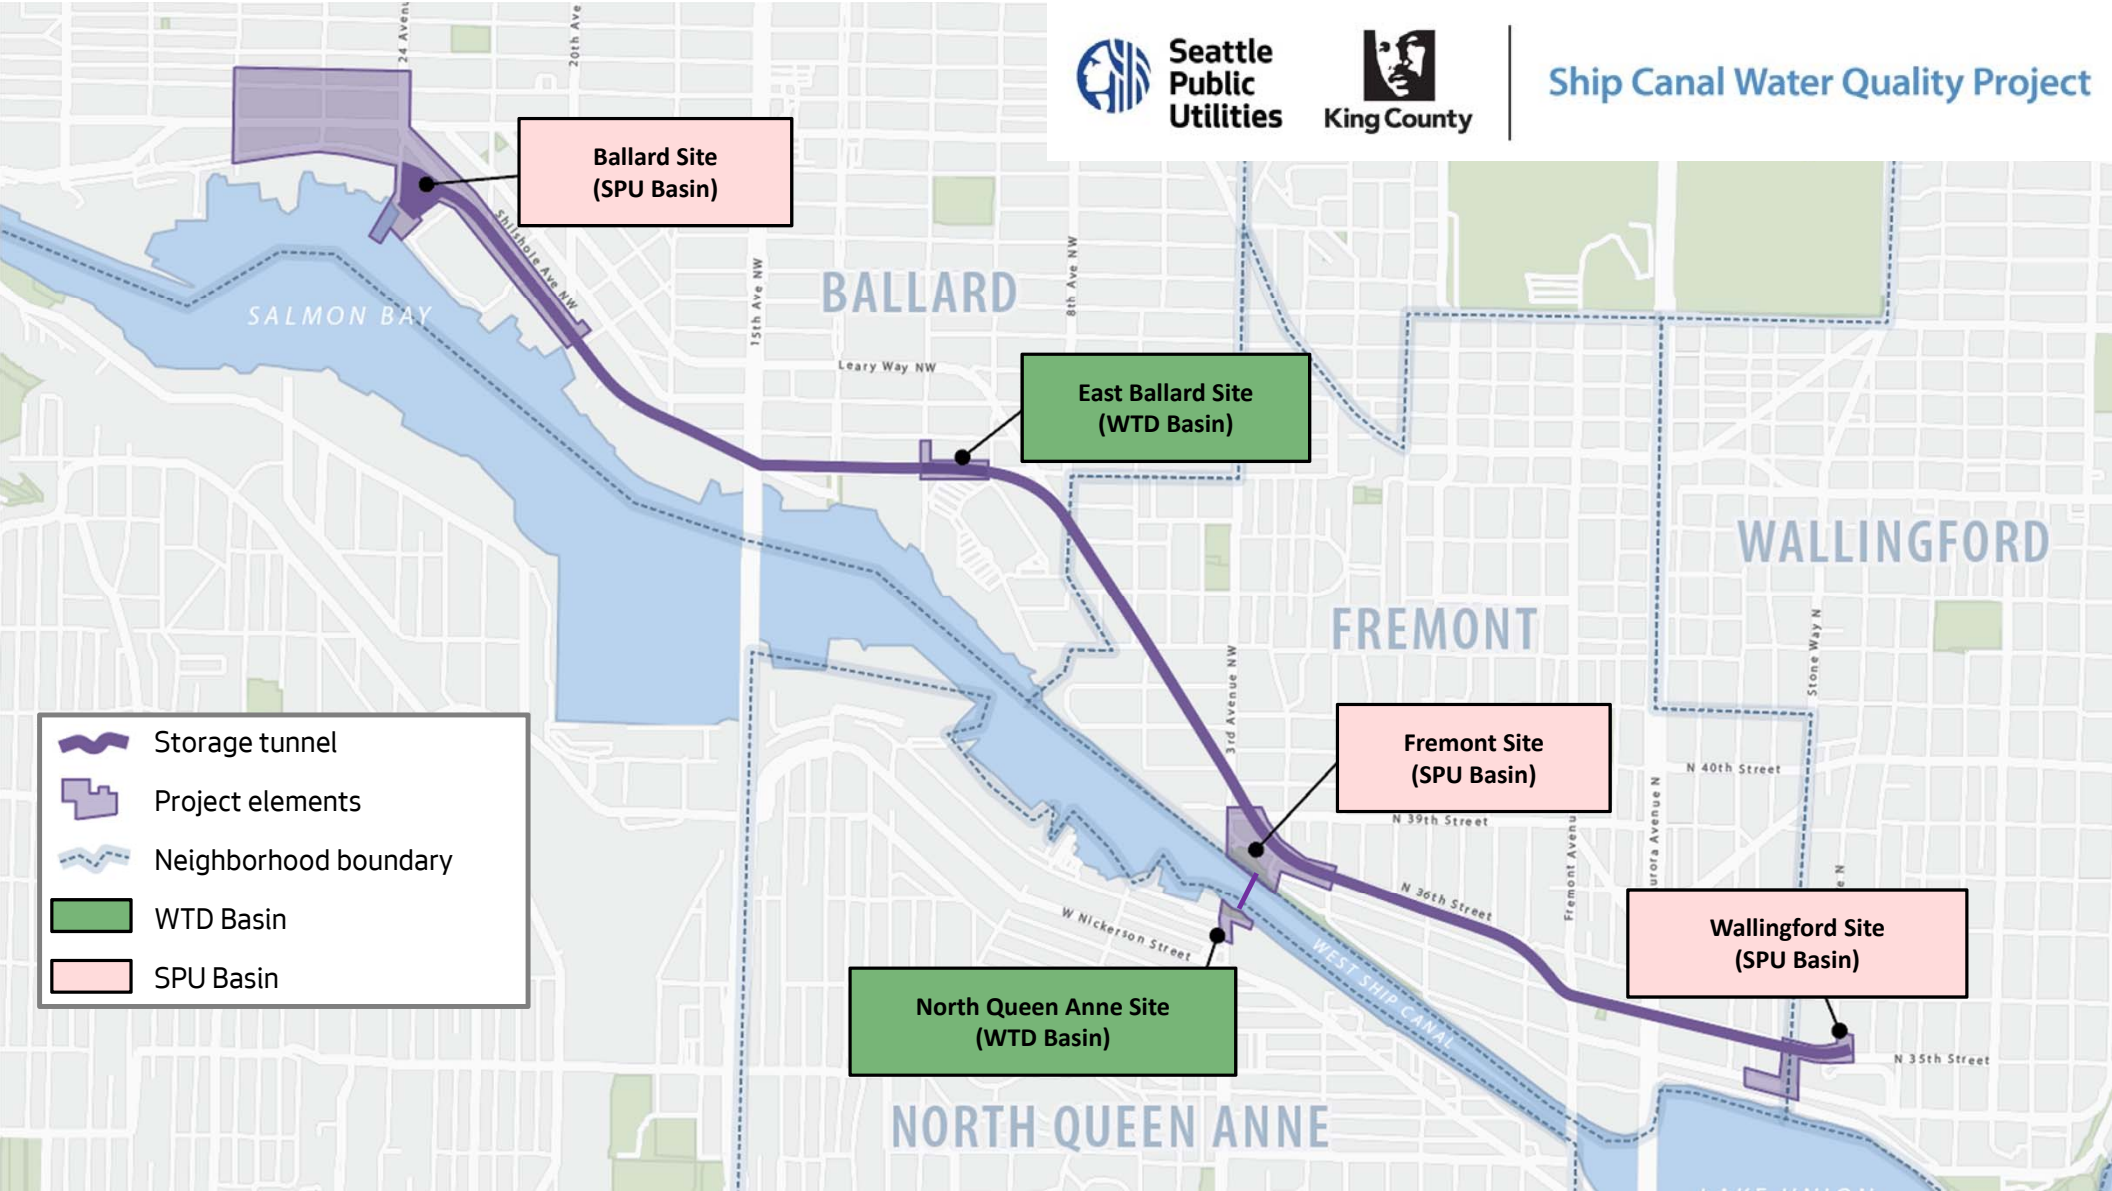


# Project Components

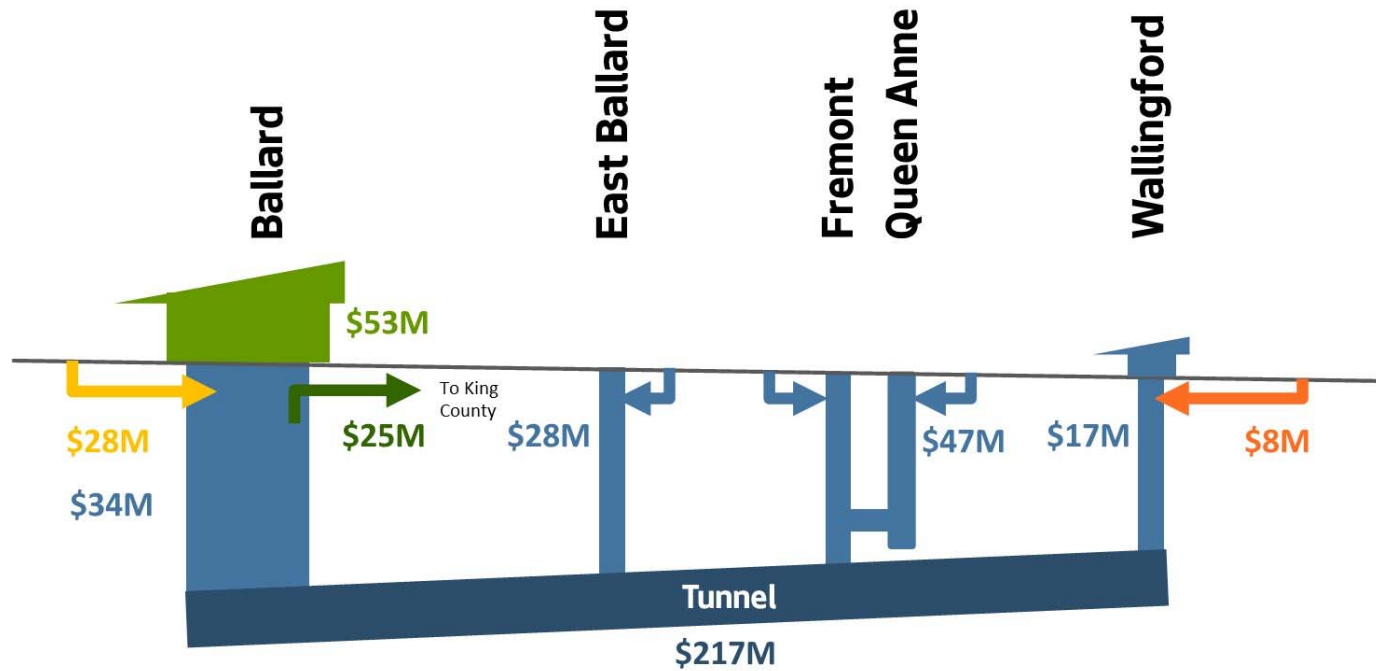


# Project Components - examples

**Fremont  
Drop  
Shaft**

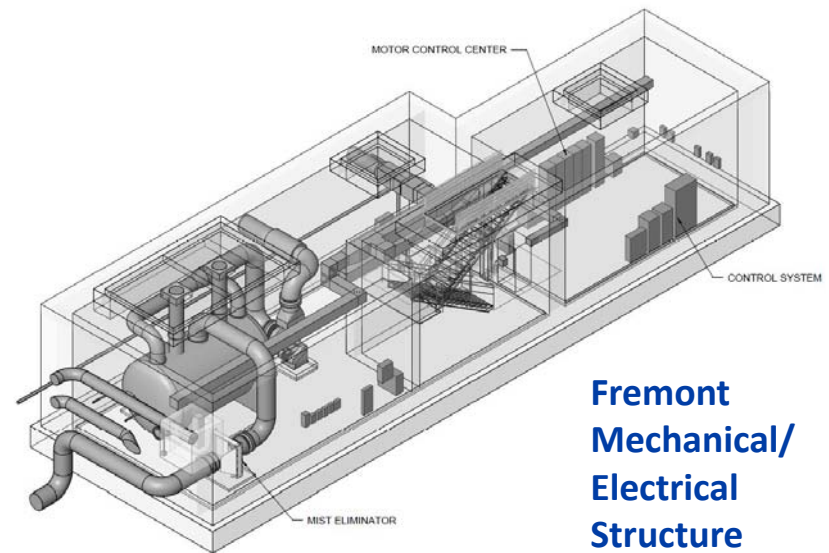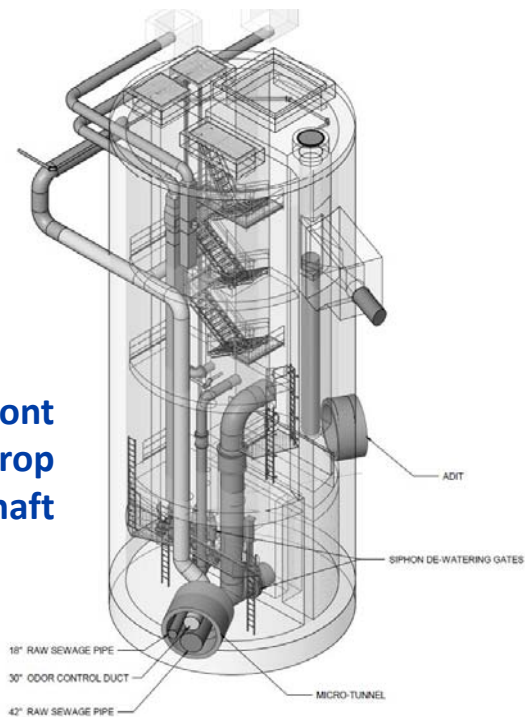

**Fremont  
Mechanical/  
Electrical  
Structure**

# Project Schedule

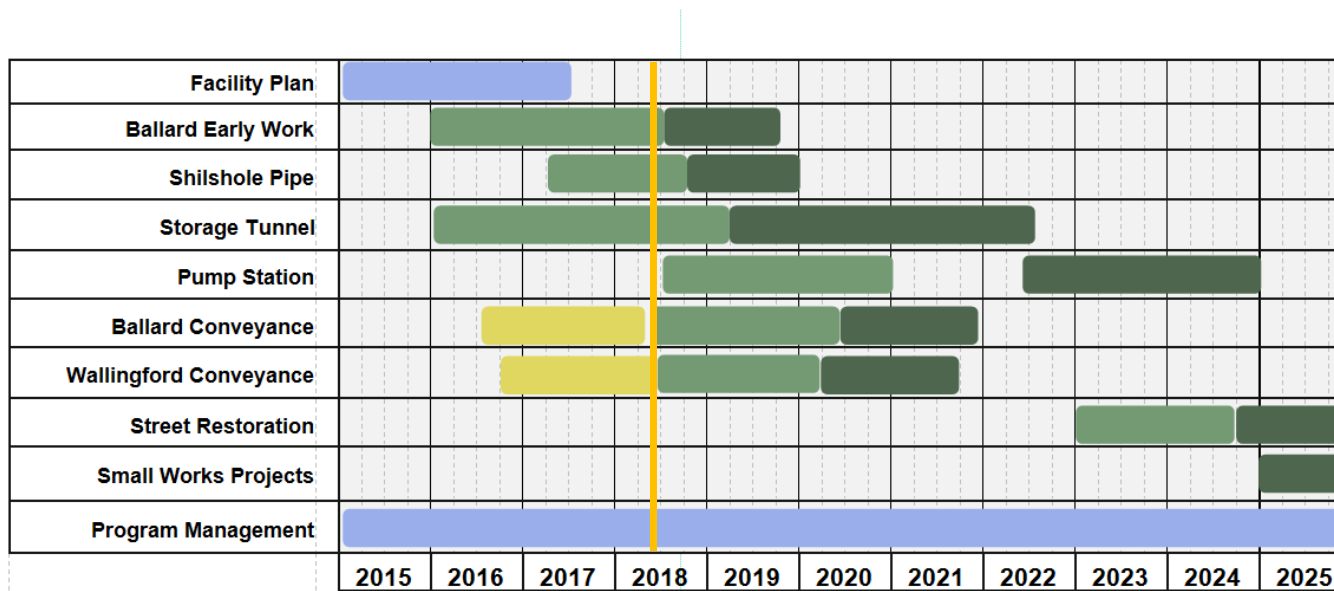

■ Planning and Management
 ■ Options Analysis
 ■ Design
 ■ Construction




# Cost Estimate - Key Steps

Year	Milestone	Level of design definition	Cost estimate or change
2014	Facility Plan	2 to 5% Design	\$423M (\$338M to \$550M range)
2015-2017	Scope and cost reductions	2 to 60% Design	(-\$35M reduction)
2017	Anticipated tunnel volume & escalation increases	5 to 90% Design	(+ \$45M to \$80M increase)
2017	Strategic Business Plan & approved budget	5 to 90% Design	\$540M
2017-2018	Cost estimate review and reconciliation process	10 to 95% Design	\$570M with a 65% confidence (\$533M to \$598M range)



# Cost Estimate Review and Reconciliation Process

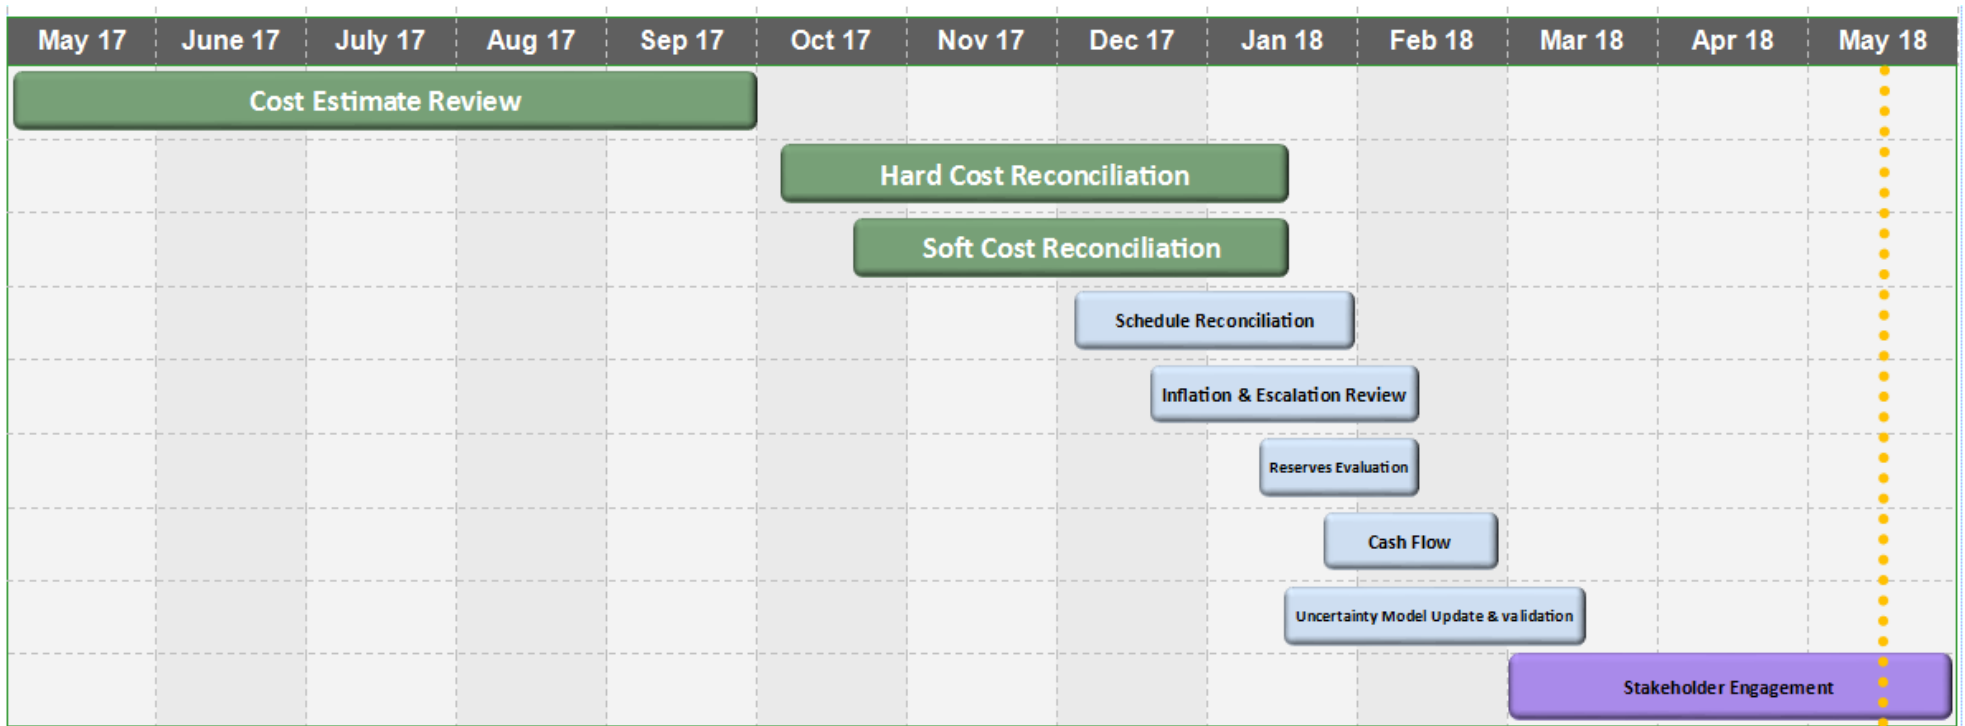

# Cost Estimate - Key Factors



**escalation**

**uncertainty**

**risks**

# Potential Scope Adjustments & Risks

Potential cost reductions found in the past two months

Scope element		Estimated Cost *	
A	Previous cost reductions	-\$34.8M	
B	Tax exemption	-\$22M	
Scope element		Estimated Cost *	Risks
1	Tunnel bid alternative	-\$8M	Complies with regulatory requirement but reduces operational flexibility
2	Use of selective refurbished Tunnel Boring Machine	-\$2.5M	Possibly reduced tunnel boring machine performance
3	Pump Station Value Engineering Recommendations	-\$4M	May not fully be able to realize the potential cost savings
4	No odor control at 3rd, Fremont, and 11 <sup>th</sup> Sites	-\$1.5M	Need to phase in equipment if there are future odor complaints
5	Construction of Wallingford and Ballard Conveyance projects earlier	-\$1M	Defers other projects and may be offset due to escalation on other projects
6	SDOT Street Use Permit Credit	-\$3M	None
7	Construction staging cost reduction	-\$0.8M	May be reflected in slightly higher bid costs
<b>Total</b>		<b>-\$20.8M</b>	

\* = Estimates need to be verified by engineering and modeling



# Cost Estimate: \$570M with 65% confidence\*


Cost Categories	New Budget Estimate with Reductions (\$M)	
Base Costs (Hard + Soft + Property) & Change Orders	\$467	
Escalation	\$60	
Cost Reductions due to Scope Changes	-\$21	
Cost Uncertainty	\$16	
Risk Costs	\$34	
Schedule Risk Impact Costs	\$14	
Schedule Risk Impact Escalation	\$0	
<b>Subtotal Cost Projection/% Confidence</b>	<b>\$570**</b>	<b>65%</b>
SRF Loan Savings - Revenue to DWW Fund	-4	

\*If all potential scope reductions are achieved, there is a 65% chance costs will be at or below the estimated cost and a 35% chance the estimated cost will be exceeded. A cost range of \$533M to \$598M is recommended around the \$570M budget.

SPU's share is approximately \$393M.

\*\*Joint Project Agreement: City of Seattle – 65%, King County – 35%

# 2014 to 2018 Variance: \$423M to \$570M\*

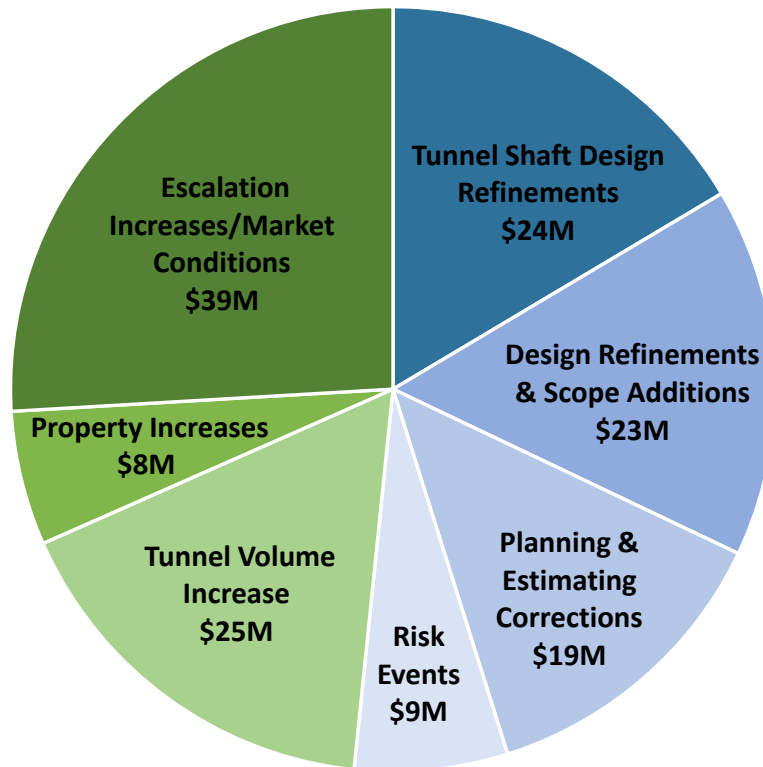

\*\$570M with a 65% confidence and a cost range of \$533M to \$598M with potential scope reductions realized.

# Project Funding

- \$540M Cost Estimate included in 2017 Strategic Business Plan and SPU's budget
- Bond Issue interest savings
- Grants and loans



# Next Steps

- Semi-annual reports
- Proviso
- Capital Cabinet







**Seattle  
Public  
Utilities**



**King County**

**Ship Canal Water Quality Project**

